

FAQ

Milestone Constraint Feeding Chain Duration


A-dato

High Performance Delivered

Milestone Monitoring and Management (1)

Milestone “Feeding Chain Tasks”

2

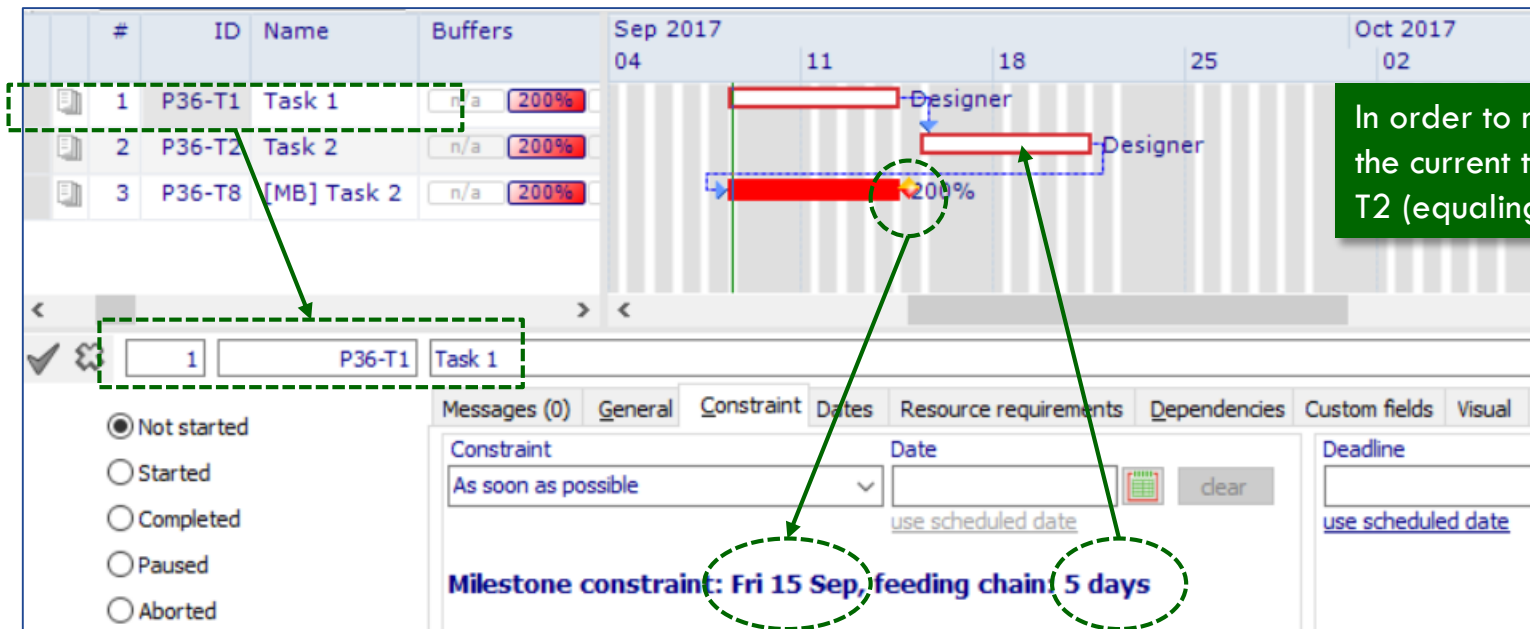

In order to meet the deadline of 15 September the current task T1 need to be completed + task T2 (equaling a feeding chain of 5 days)

With this information the Project Manager has visibility of the duration of the total chain still to be completed → if the deadline need to be moved can better estimate what a new realistic date should be.

My activities

Milestone Constraint Management and Monitoring

3

The screenshot displays a software interface for task management. At the top, there are navigation tabs: "My activities", "Messages (0)", "Project portfolio", "Active tasks", "Calendar", "Configure", and "Reporting". Below these is a search bar containing "fee" and a "Cards >>" button. A table lists tasks with columns for ID, Description, Task type, Milestone constraint, TM, Priority, RTS, and Resources. One task is highlighted: ID P36-T1, Description "Task 1 Milestone Feeding Chain", Task type "Normal", Milestone constraint "Fri 15 Sep [-5 days]", TM "AC", Priority (red circle), RTS "Yes", and Resources "Designer [5 days, not started]". To the right, the "Task details" panel shows information for ID P36-T1, including description, project manager, scheduled dates, milestone constraint, and last update. Below this are tabs for "Resourcing", "Notes (0)", "Custom fields", "Working hours", and "Workpackage". The "Resourcing" tab is active, showing fields for "Your role" (Task manager), "Skill" (Designer), "Resource(s)" (Mike Dempsey), "Status" (Not started), and "Etc" (5 days/40h).

ID	Description	Task type	Milestone constraint	TM	Priority	RTS	Resources
P36-T1	Task 1 Milestone Feeding Chain	Normal	Fri 15 Sep [-5 days]	AC		Yes	Designer [5 days, not started]

Task details

ID P36-T1
Description Task 1
Project Milestone Feeding Chain
Project manager A-dato Consulting, A-dato
Scheduled dates Today 9:00 - Thu 14 Sep 17:00
Milestone constraint Fri 15 Sep [-5 days]
Last update Sat 11 Apr 2015 13:09 by A-dato Consulting
Task manager A-dato Consulting, A-dato

Resourcing | Notes (0) | Custom fields | Working hours | Workpackage

Designer

Your role Task manager
Skill Designer
Resource(s) *Mike Dempsey
Status Not started
Etc 5 days/40h
Please enter the 'expected time to complete' for this task

Milestone Monitoring and Management (2)

Milestone “Feeding Chain Tasks”

4

#	ID	Name	Buffers
1	P10-T1	Validation of Concept	0% 0% n/a
5	P10-T4	Review of Concept	0% 0% n/a
6	P10-T5	External design	0% 0% n/a
7	P10-T6	Build 2a	0% 0% n/a
8	P10-T7	Integration 2	0% 0% n/a
9	P10-T158	Milestone buffer	n/a 0% n/a

Milestone constraint: Fri 13 Jan 2017 19:30, feeding chain: 13 day

Milestone constraint: Fri 13 Jan 2017 19:30, feeding chain: 4 days

After completing T1, still 13 days Feeding Chain Tasks towards the Milestone remain:
 (T4(3d)+ T5(3d) + T6(3d) + T7(4d))

My activities

Milestone Constraint Management and Monitoring

5

The screenshot displays a software interface for task management. On the left, a table lists tasks with columns for ID, Description, Start date, Milestone constraint, Priority, and RTS. The first row, 'P10-T1 Validation of Concept', is highlighted with a dashed green box. A green arrow points from this row to the 'Task details' panel on the right. The 'Task details' panel shows information for 'ID P10-T1', including description, project, manager, scheduled dates, and milestone constraint. The 'Milestone constraint' field is also highlighted with a dashed green box. Below the details, there are tabs for 'Resourcing', 'Notes (8)', 'Documents (0)', 'Custom fields', and 'Working hours'. The 'Designer' section shows the role 'Resource Mike Dempsey', skill 'Designer', and resource '* Mike Dempsey'. The status is 'Not started' and the effort is '5 days/40h'. The expected completion is 'Thu 15 Dec 17:00 at 100%'.

ID	Description	Start date	Milestone constraint	Priority	RTS
P10-T1	Validation of Concept D3 Product development	Today 9:00 [w49]	Fri 13 Jan 2017 19:30 [-13 days]	High	Yes
P10-T10	Assembly D3 Product development	Wed 4 Jan 2017 9:00 [w1]		Medium	No
P10-T11	Final Test D3 Product development	Tue 10 Jan 2017 9:00 [w2]		Medium	No

Task details

ID P10-T1
Description Validation of Concept
Project D3 Product development
Project manager A-dato Consulting, A-dato
Scheduled dates Today 9:00 - Thu 15 Dec 17:00
Milestone constraint Fri 13 Jan 2017 19:30 [-13 days]
Last update Mon 25 Jul 10:56 by A-dato Consulting
Task manager Robin Porter, LYNX GmbH
Sven Cramer, A-dato

Resourcing Notes (8) Documents (0) Custom fields Working hours

Designer

Your role Resource Mike Dempsey
Skill Designer
Resource(s) * Mike Dempsey
Status Not started
Ettc 5 days/40h
Please enter the 'expected time to complete' for this task
Expected completion Thu 15 Dec 17:00 at 100%
